

Project Change Order



4/5/2023

Plug Smart, an Ameresco Company
640 Lakeview Plaza Blvd. Suite J
Columbus, Ohio 43085


Client: Buckeye Local School District
Project: AC Addition Project
RE: **Ridgeview Kindergarten Classrooms**

This is a: Changes in Scope (Functionality)
 Change in Implementation Schedule/Delivery Dates
 Change from Estimated Budget

Description of Change(s) requested:

The contract changes include the following:

- Add the following classrooms to the scope of work to receive mini splits for space cooling. The equipment needed will be two 4-ton condensing units, four 2-ton indoor units, all line hide, line sets, and any other material needed to provide a fully operational system.
- The price below is turnkey and includes electrical, installation, material procurement, project management, drawings and permit revisions.
- This addition and the delays from the utility company will increase the substantial completion date from 4/15/23 to 5/31/23.

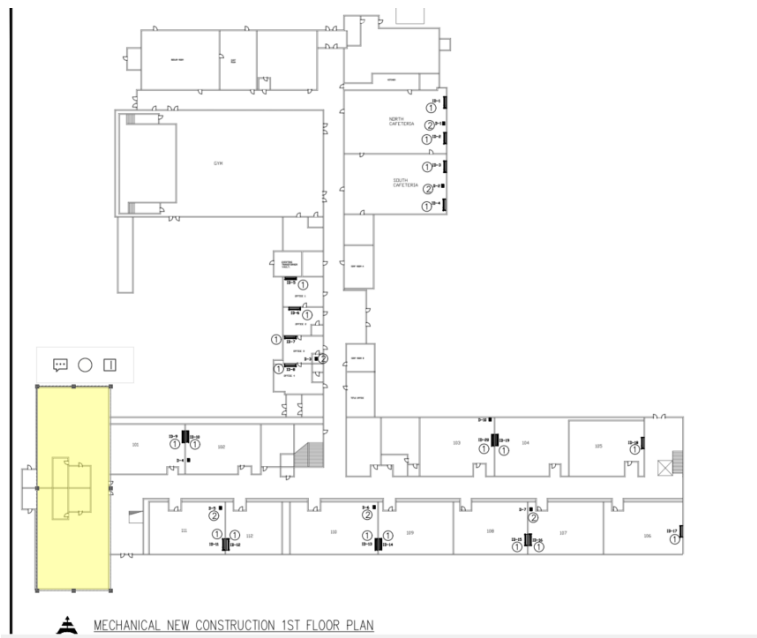

Cost:

- \$33,592.00

Contract Summary

- Original Contract Value: \$ 1,490,292.00
 - Previous Change Orders: \$ 0.00
 - This Change Order \$ 33,592.00
- Revised Contract Amount: \$ 1,523,884.00**

Approval:

Ameresco Manager: _____ **Date:** _____

Client: _____ **Date:** _____
